

Tree protection plan
Location of trees, categorisation & protection/management proposals










Camps Road (opp CRL Development), Haverhill, Suffolk

Barrell Plan Ref: 19351-3



Permission is granted to scale from this drawing for Local Authority Planning Approval purposes relating to tree protection measures only. Where applicable this drawing is to be read in conjunction with the arboricultural report. This drawing is the copyright of Barrell Tree Consultancy 2021. ©

This drawing to be reproduced in colour only.
www.barrelltreecare.co.uk


-  BS category B Trees of moderate quality
-  BS category C Trees of low quality
-  Trees to be removed
-  Proposed layout
-  Protective barrier/fencing
-  Construction exclusion zone (CEZ)
-  Precautionary area where new surfacing will be installed using a cellular confinement system and a new base to accommodate the substation.
-  Root protection area (RPA) boundaries for category B trees
-  Root protection area (RPA) boundaries for category C trees

This drawing contains:
Topo = (November-27-2019) SU-01
Layout = (June-16-2021) 40033HH-PL02



Tree No	Species	Category	RPA Radius	Tree Works
All retained trees				Carry out safety check and lift over site to 3-4m as necessary.
T40	Lime	B	5.4	-
T41	Sycamore	B	6.0	-
T42	Lime	B	7.8	-
T43	Beech	C	6.0	-
T44	Lime	B	6.0	-
T45	Holly	C	3.0	Fell
T46	Holly	C	3.6	Fell
T47	Lilac	C	2.4	Fell
T48	Sycamore	B	5.4	-
T49	Holly	C	2.4	-
T53	Cypress	C	2.4	Fell

SGN 1 Monitoring tree protection

-  **Always:**
- ✓ have a pre-commencement meeting with the tree consultant before development starts
 - ✓ use the tree consultant to regularly check that protection remains fit for purpose
 - ✓ use the tree consultant to supervise work in RPAs
 - ✓ keep a written record of supervision




SGN 2 Fencing protected trees

-  **Always:**
- ✓ install protection before development starts
 - ✓ make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
 - ✓ keep protection in place until there is no risk to trees
 - ✓ get written permission to move or remove any protection




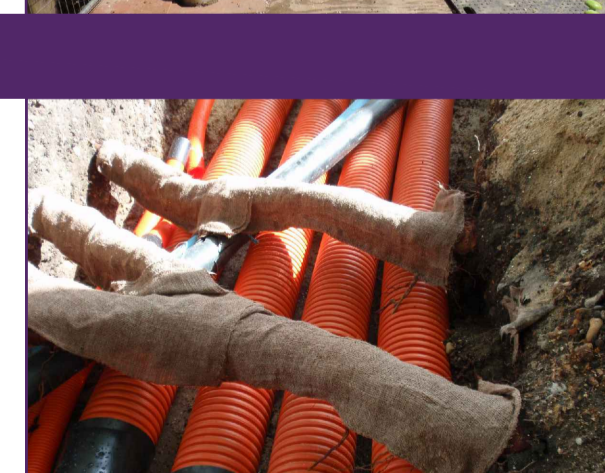
SGN 3 Ground protection

-  **Always:**
- ✓ install protection before development starts
 - ✓ make sure protection is fit for purpose, i.e. it prevents damage to trees and soil
 - ✓ keep protection in place until there is no risk to trees
 - ✓ get written permission to move or remove any protection

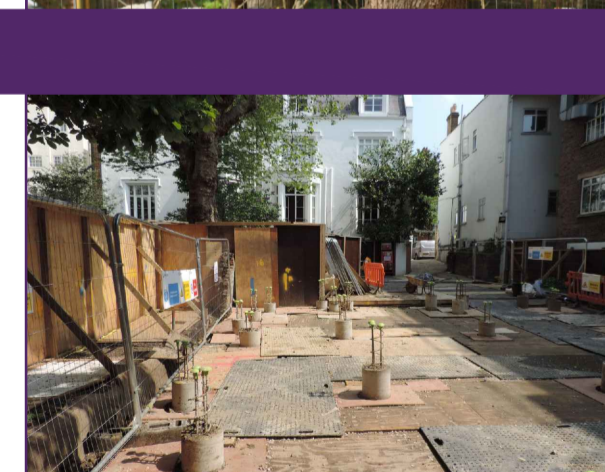

SGN 11 Installing services in RPAs

-  **Always:**
- ✓ use the tree consultant to supervise work in RPAs
 - ✓ select the least damaging option when installing services, so prioritise trenchless, over broken trench over continuous trench
 - ✓ hand-dig trenches if trenchless is not feasible



How to use plan

More detailed guidance on each Site Guidance Note (SGN) can be found in a printed hard copy compilation of all the SGNs, **Manual for Managing Trees On Development Sites version 2.1**, issued to the Site Manager at the pre-commencement site meeting (Note: This should be retained on site throughout the duration of works). Additionally, an electronic pdf compilation of all the SGNs, was submitted with this drawing to the local planning authority and the client. Alternatively, a pdf of each SGN can be downloaded by:

1. clicking the image links in the electronic pdf version of this plan;
2. holding a mobile phone QR (Quick Response) code reader over the QR code in the paper version of this plan; or,
3. visiting our website at <https://www.barrelltreecare.co.uk/resources/technical-guidance>
